

ANSA McAL Group

Factorial IT Implementation Package

~6,000 employees · 48 operating companies · Caribbean

Systems: Factorial IT · SAP SuccessFactors · Microsoft 365

Commercial: POC ~500 employees / ~1,000 devices · target ~10,000 devices by June 2027 · kick-off October 2026 · Professional Services **USD 5,000 once** at kick-off · platform billing from January 2027

1. Scope

Factorial IT will operate ANSA McAL's IT asset lifecycle: request, approval, procurement, registration, deployment, transfer, recovery, retirement and disposal. SAP SuccessFactors remains the system of record for people and organisation data.

In scope	Out of scope
ITAM / inventory; MDM; JML automation; procurement and catalogue; SaaS / licenses; asset ticketing; remote assistance; approvals; reporting; audit trail.	Payroll / core HR; ITIL incident & problem management; SLA timers; change management; CMDB impact modelling; network redesign; non-IT facilities assets; Android corporate Zero-Touch; native buyback/payment workflow; signature / acceptable-use capture.


Android: BYOD Work Profile in scope. Company-owned Android uses staged provisioning (not Zero-Touch).

Disposal: ANSA nominates local disposal vendors; Factorial IT carries the evidence trail.

POC: mandatory gate before January 2027 go-live (macOS, Windows, iOS, Android BYOD + company-owned).

2. Target Architecture

Figure 1 — System context (one-way people data; Factorial IT as asset operations hub)

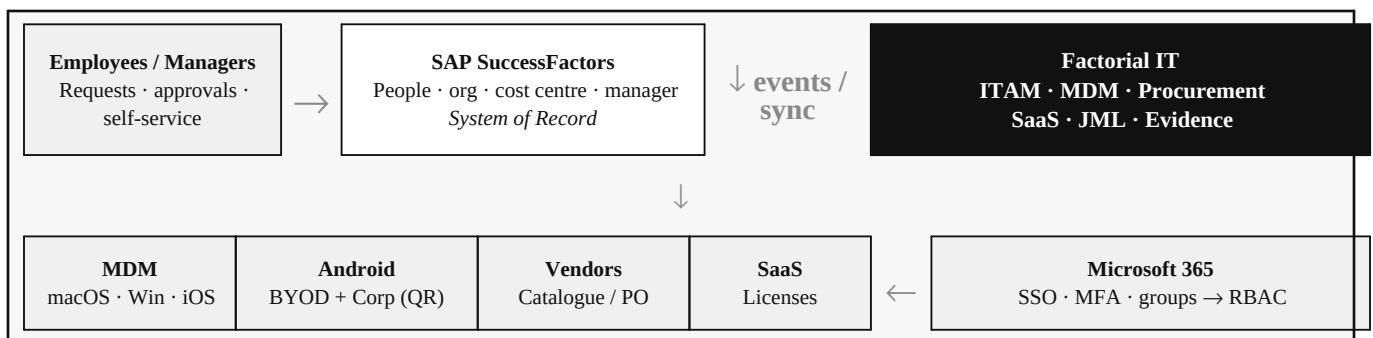


System of record: SuccessFactors for people data. Operational system of record: Factorial IT for asset operations.

3. Core Flows

Joiner / Mover / Leaver

Figure 2 — Corporate devices on macOS / Windows / iOS: automated wipe/lock. Android: company-owned remote wipe (console) or BYOD disenrollment on termination.



Device lifecycle

	Approval Policy thresholds	Order Catalogue / PO	Register Serial / model / cost	Configure MDM baseline	Handover Onboarding record	Transfer / Offboard Reassign / wipe / recover	
--	----------------------------------	-------------------------	--------------------------------------	---------------------------	----------------------------------	--	--

4. Delivery Roadmap

Phase	Timing	Outcome / gate
0 • Planning	Early Oct 2026	Charter and governance
1 • Discovery	Oct 2026	Signed inputs and OS estate split
2 • Design + Configure	Oct–Nov 2026	Solution design, RBAC, catalogue, workflows, MDM
3 • Integration + POC	Nov–Dec 2026	SuccessFactors sync + four OS paths validated
POC Gate	Dec 2026	Steering sign-off required
4 • Go-live	Jan 2027	~500 employees / ~1,000 devices
5 • Rollouts	Jan–Jun 2027	Cohorts expand to ~10,000 devices
6 • Hypercare / BAU	From Jun 2027	Stabilisation and handover

Rollout sequence



5. Discovery Workshops

Workshop	Output
Asset Governance	Lifecycle states, mandatory fields, evidence; ANSA nominates local disposal vendors
Procurement & Catalogue	Equipment Policy, Purchasing Policy, country catalogues
Joiner / Mover / Leaver	Event-to-automation design
Security & Compliance	MDM baseline, RBAC, retention
Identity & SSO	IdP, SSO, SCIM decisions
MDM Operations	OS enrolment paths; Android Work Profile / staged provisioning
SaaS & Licenses	Register, approval and reclamation rules
Reporting	KPI / dashboard definitions
SuccessFactors Integration	Field map, event contract, error handling

6. Key Capability Outcomes

Area	Target state
Joiner	Hire event opens onboarding and applies equipment entitlement
Leaver	Termination drives access deprovisioning, device action and recovery
Transfer	Company / cost centre / manager updated with configured approvals
Procurement	Purchasing Policy controls catalogue spend and approvers
Disposal	Closure requires disposal / wipe evidence
MDM	Unified management for macOS / Windows / iOS; Android BYOD Work Profile in Phase 1
SaaS	Central register, approvals and reclamation rules
Audit	Single evidence trail across asset events


Boundaries: Android corporate Zero-Touch is not Phase 1. Signed handover / acceptable-use acknowledgement remains outside the platform. Staff buyback runs as a ticket, with valuation and Finance approval outside the platform.

7. Commercials

All figures in USD.

Item	Terms
Platform list price	USD 10 / managed device / month
ANSA offer	USD 6 / managed device / month for initial 12 billable months
POC / ramp	~1,000 devices initially; target ~10,000 by June 2027; quarterly true-up
Oct–Dec 2026	Platform complimentary
First platform invoice	January 2027
Professional Services	USD 5,000 fixed
PS payment	USD 5,000 once at kick-off (October 2026)
Minimum subscription term	12 billable months: Jan–Dec 2027

Figure 4 — Commercial timeline (USD · October start)



Year-1 snapshot: Platform Jan–Dec 2027 ≈ USD 549,000 under the stated ramp assumption + USD 5,000 implementation = ≈ USD 554,000 total.

8. Included

Platform	Professional Services (USD 5,000)
• ITAM / CMDB • MDM connectors (macOS, Windows, iOS, Android BYOD + company-owned wipe) • Asset ticketing & remote assistance • JML automations • Procurement / catalogue • SaaS visibility • Approvals & audit trail	• Phases 0–3 POC delivery • 9 discovery workshops • SuccessFactors integration design & build support • POC validation and go-live readiness • Rollout runbooks & training foundation

Final gate: Steering Committee POC sign-off is required before January 2027 production go-live.
